Final bill

Recorded on:-12/12/18

Work Code No:-002-18-000029

M. A. R. 57 (Rule 116)

Measurement Book

No. B Est Cost: 25.00 Lakhs

Work order No:- EE (YNK-D) E-PMT-02/W.O/73/2018-2019 466628

No. .....

of Work ... Improvements to drains at Kondappa Layout in Ward No-02 of Yelahanka Sub Division From ... To ...

of Contractor of nature of Agency ... Sri. Prakash Naik, No:313, Veerannapalya, Anafic College post, Bangalore.

f commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
KSRB 2-2.1: Earth work excavation for foundation of buildings, culverts water supply, Sanitary line and electrical conduits either in pits or in trenches 1.5m and above in width in ordinary soil not exceeding 1.5m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead up to 50m, after breaking of clods Complete as per Specifications.						
Quantity vide, As per pre-measurement recorded in this unit and page No of:- 466668-69:- 301.96 m^3						
						G2807.68
					CRS. 208.00	

Scanned by CamScanner

M. A. R. 57 (Rule 116)
Measurement Book

No. B

466630

. .....
Work ..... From..... To.....
Contractor of nature of Agency .....
commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
Drain Bottom Concrete:-						
Koondoppa Layout 9th						
Gross:-	1	16.50	0.75	0.15	1.85	
	1	8.90	0.75	0.15	1.00	
	1	30.00	0.75	0.15	3.37	
	1	3.60	0.75	0.15	0.40	
:-	1	21.50	0.75	0.15	2.41	
:-	1	25.00	0.75	0.15	2.81	
13th 'c' Gross:-	1	30.00	0.90	0.15	4.05	

Scanned by CamScanner

M. A. R. 57 (Rule 116)
Measurement Book

No. B

466631

No. .....
of Work ..... From..... To.....
of Contractor of nature of Agency .....
f commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
Side walls:-						
Kondappa Layout 4th Gross:-	2	16.50	0.15	0.50	2.47	
	2	8.90	0.15	0.50	1.33	
	2	30.00	0.15	0.50	4.50	
	2	3.60	0.15	0.50	0.54	
:-	2	21.50	0.15	0.50	3.22	
:-	2	25.00	0.15	0.50	3.75	
13th 'C' Gross:-	2	30.00	0.15	0.60	5.40	

Scanned by CamScanner

M. A. R. 57 (Rule 116)
Measurement Book

No. B 466632

No. .....
of Work ..... From..... To.....
of Contractor of nature of Agency .....
of commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
	2	14.00	0.15	0.60	2.52	
					91.41 m³	10,48,838.34
Cost Index 2018					@ RS. 11474.00	
(5) KSRB 5.2.3: Providing and Constructing granite/trap/basalt Size stone masonry in foundation with Cement mortar for 1:6 stone hammered dressed in Courses not less than 20 Cms high, bond stones at two mts. apart in each Course including Cost of materials labours, Curing Complete as per Specifications.						
S.S.M Division, Hs:	1	8.50	0.60	0.40	2.04	
	1 x 1.20 x 0.60 x 0.60 =				0.43	

Scanned by CamScanner

M. A. R. 57 (Rule 116)
Measurement Book

No. B 466637

Work ..... From..... To.....

Contractor of nature of Agency .....

ommencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8

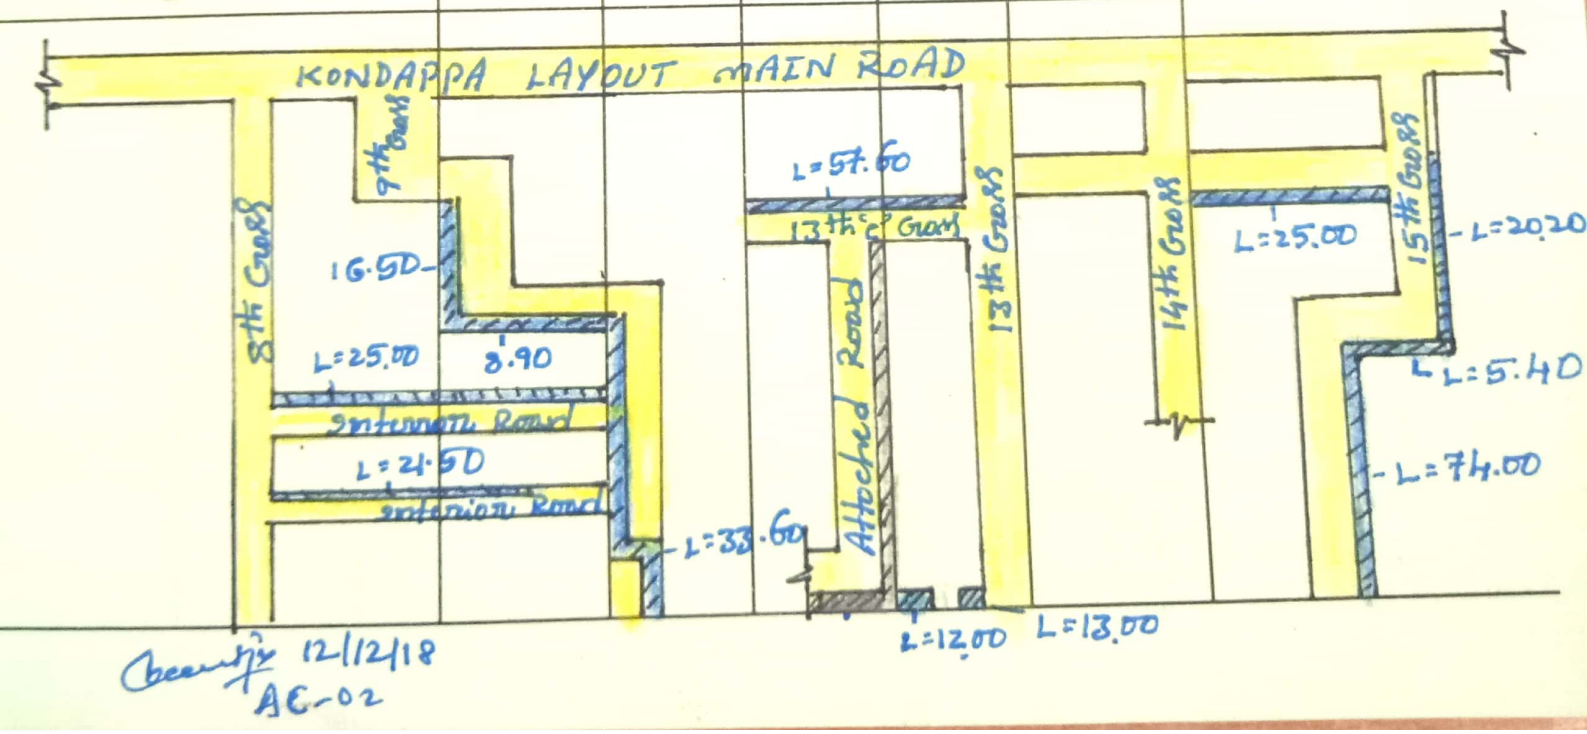

Checked 12/12/18
AE-02

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	
		3	1.50	0.60	-	2.70	
						18.54 m²	
	Limited to Schedule 'B' :					18.00 m²	
						@Rs. 4450.00	80,10
			Total Bill Amount			Rs=	259,4

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP Ynk. Zn)
Yelahanka, Bangalore

12/12/18
AE-02

CERTIFICATE :-

1) Certified that the above work done is satisfactory leted

2) Certified that the There is no debries have been cle to site.

12/12/18
AE-02

Scanned by CamScanner
